


Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

SRN: PES1UG24CS655 | Name: Arjun Bhat | Section: K | Date: 28 Aug 2026

1. Epics and User Stories (Backlog)

I took the functional requirements from Lab 1 (the domain / SSL certificate monitoring system) and turned them into 5 Epics, one for each FR. Each Epic has 2 user stories, so 10 stories in total. The Epics are: FR-001 SSL/TLS Certificate Checking, FR-002 WHOIS Domain Check, FR-003 Manage Monitored Domains, FR-004 Store Audit Results and FR-005 Generate Expiry Alerts.

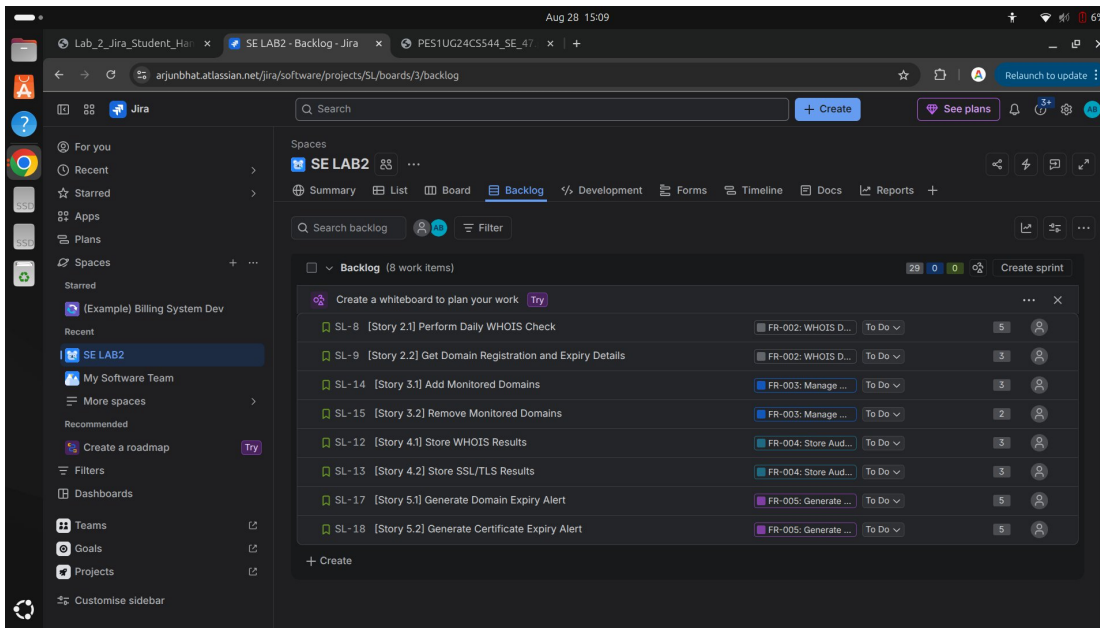





2. Story Points

I used the Fibonacci scale for estimating. Estimates were: Story 1.1 = 8, Story 1.2 = 5, Story 2.1 = 5, Story 2.2 = 3, Story 3.1 = 3, Story 3.2 = 2, Story 4.1 = 3, Story 4.2 = 3, Story 5.1 = 5, Story 5.2 = 5. That is 42 points overall. The story points are visible in the backlog screenshot above.


3. Sprint Board

Sprint 1 had 4 stories (SL-5, SL-6, SL-8, SL-9), 21 points. I moved them from To Do to In Progress to Done.

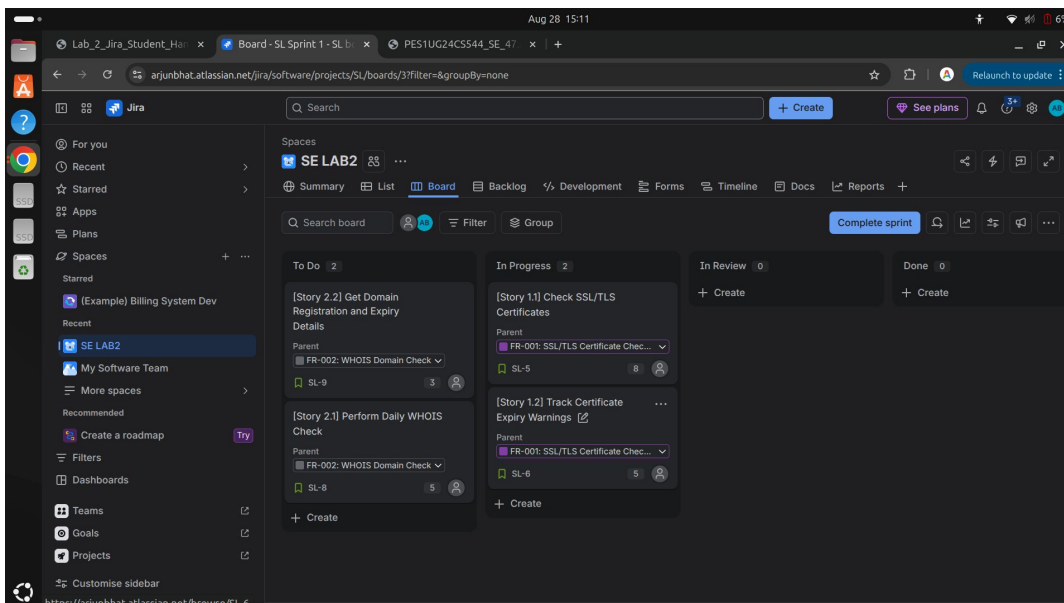

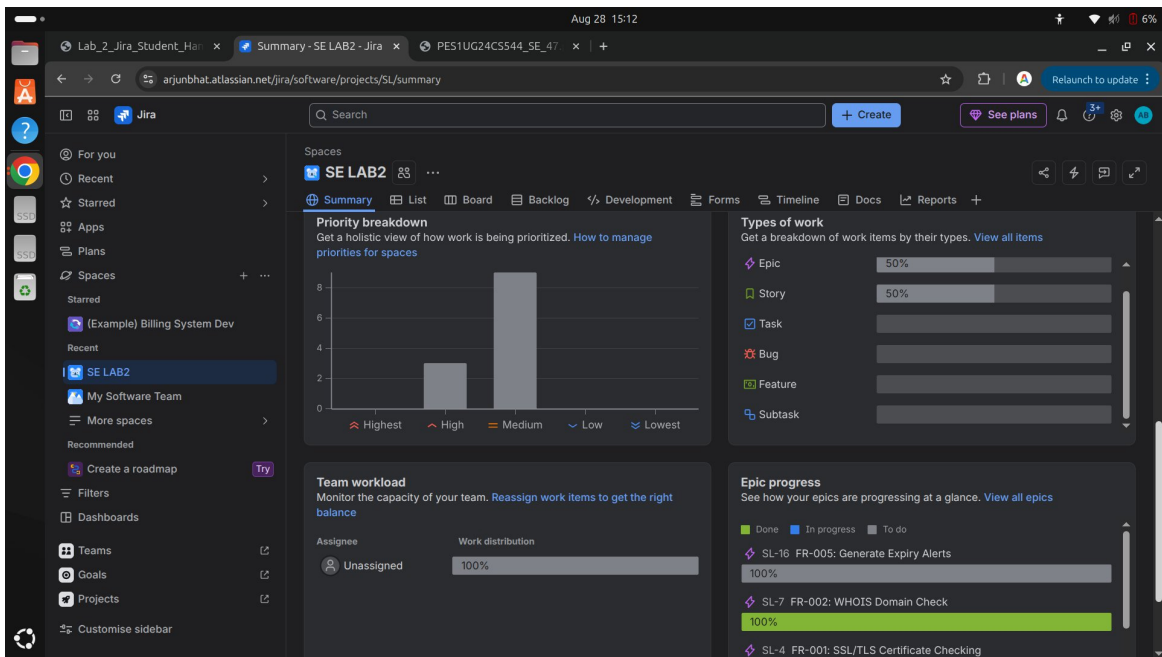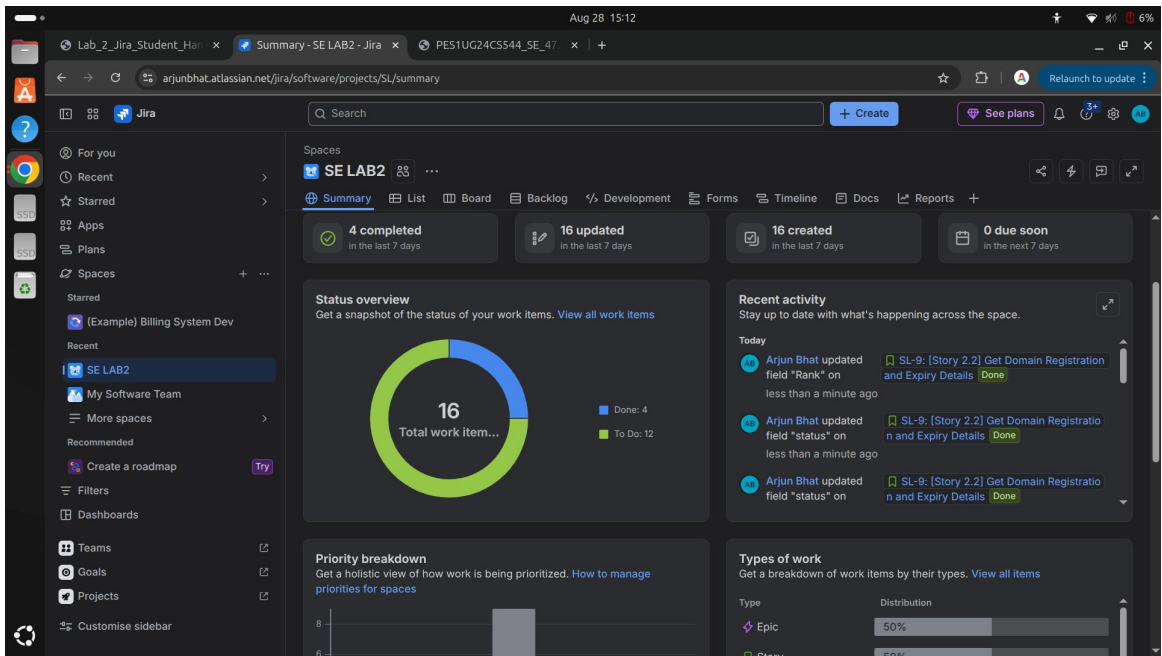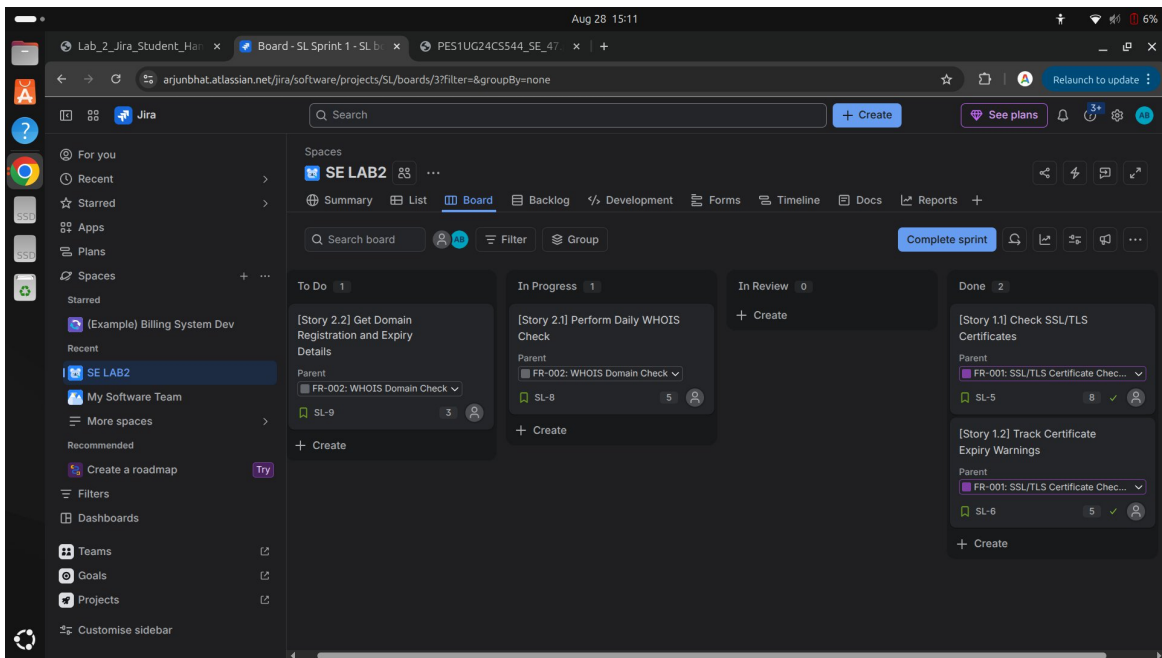

4. Burndown Chart

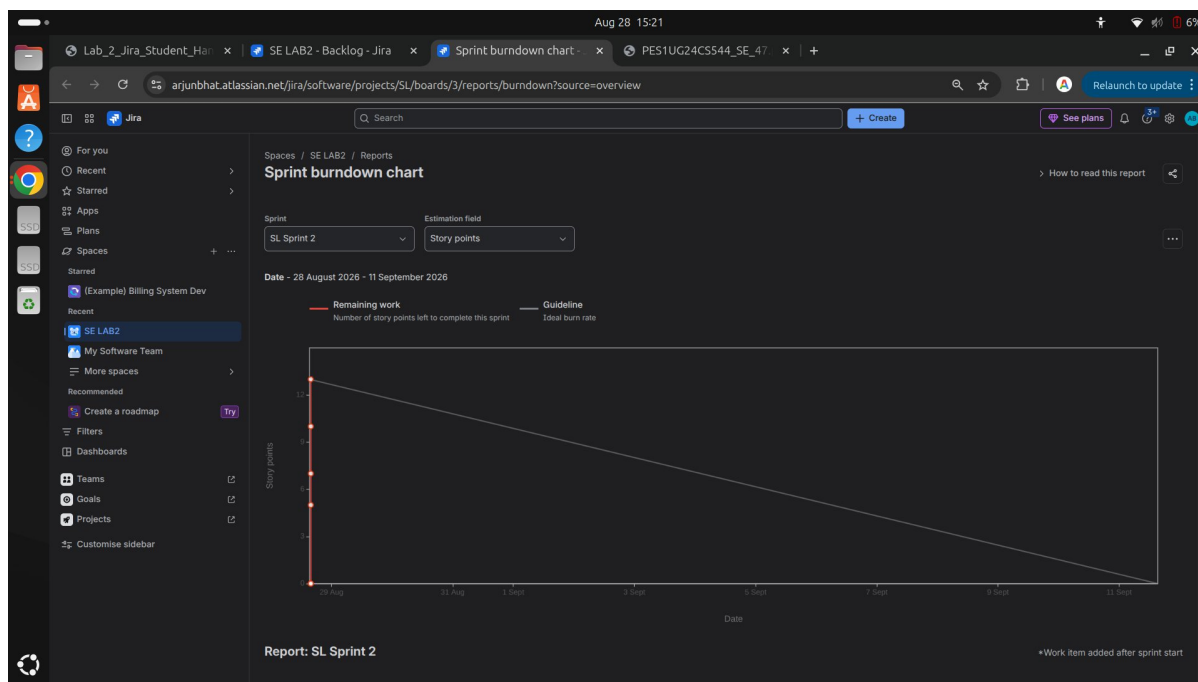

5. Reflection Questions

1. Did your estimations reflect the actual effort?

Not really, mainly because this was a simulation. Since nothing was actually built, I moved the cards after a few minutes, so the actual effort was almost the same for every story regardless of its points. However, the estimates were reasonable relative to each other. For example, checking SSL/TLS certificates (8 points) involves more work than removing a monitored domain (2 points) because of network calls and error handling. In a real project, I would compare estimates with the actual time taken and adjust them. The 8-point story could also have been split into smaller stories.

2. Was your backlog well-prioritized?

Mostly yes. I placed core features like certificate and WHOIS checks in Sprint 1 because other features depend on them. However, most stories were Medium priority, so the priorities were not very spread out. I could have used Low and High priorities more clearly. Also, "Add Monitored Domains" should probably have been earlier since domains are needed for the checks.

3. How did your simulated sprint align with your plan?

Sprint 1 went as planned, with all 4 stories (21 points) completed. Sprint 2 was also completed successfully. However, the simulation was much smoother than a real project because everything was completed within minutes. The handout specified 1-week sprints, but Jira shows Sprint 2 as 28 Aug to 11 Sept, which is two weeks, likely because I left the default duration. There were also no blockers, scope changes, or carry-over stories, which would be unusual in a real project.

4. What insights did the burndown chart give about your team's capacity?

The red line drops almost straight from around 13 points to 0 because I marked the stories as Done at nearly the same time. This does not represent a typical burndown, but it shows the work was completed early. The sprint had about 13 points compared to 21 in Sprint 1, so the velocity is not consistent yet. More sprints would be needed to estimate the team's actual capacity. Overall, the chart helped me understand burndown, but real project data would be needed for accurate conclusions.
